


ID	Task	Task Name	Duration	Start	Finish
1		Highway Village S&R Water Mains	302 days	Mon 6/27/22	Mon 9/11/23
2		Preconstruction Noticing	132 days	Mon 6/27/22	Thu 1/12/23
3		NTP	0 days	Mon 6/27/22	Mon 6/27/22
4		Material lead times	118 days	Mon 6/27/22	Fri 12/16/22
5		Material delay	0 days	Thu 1/12/23	Thu 1/12/23
6		[REDACTED]			
7		[REDACTED]			
8		Preconstruction Video & Photos	1 day	Mon 1/2/23	Mon 1/2/23
9		24Hr Notification	0 days	Tue 1/3/23	Tue 1/3/23
10		Mobilization	23 days	Wed 1/4/23	Mon 2/6/23
11		Mobilization & SWPPP Implementation & Traffic Control	1 day	Fri 1/13/23	Fri 1/13/23
12		Record Monuments-CCS	1 day	Wed 1/4/23	Wed 1/4/23
13		Sawcut Lou Ann Dr, Brenner Way , Strivens Ave & Earl Street National Concrete Cutting	1 day	Tue 1/17/23	Tue 1/17/23
14		Installed rock bags	1 day	Tue 1/17/23	Tue 1/17/23
15		Potholing	5 days	Mon 1/23/23	Fri 1/27/23
16		Tie-In at Rumble & Install Waterline on Lou Ann Dr	3 days	Wed 1/18/23	Fri 1/20/23
17		[REDACTED]			
18		[REDACTED]			
19		[REDACTED]			
20		Brenner Way , Strivens Ave & Earl Street	46 days	Tue 2/7/23	Wed 4/12/23
21		Install Waterline, Hydrants, Bollards and Srvcs-Brenner Way , Strivens Ave & Earl Street	35 days	Tue 2/7/23	Tue 3/28/23
22		[REDACTED]			
23		Sawcut Crommelin Ave, Sparks Way & Budd St-National Concrete Cutting	1 day	Wed 3/29/23	Wed 3/29/23
24		Tie-In at Brenner Way , Strives Ave & Earl Street	3 days	Thu 3/30/23	Mon 4/3/23
25		[REDACTED]			
26		[REDACTED]			
27		2 Week Notice	0 days	Thu 3/30/23	Thu 3/30/23
28		1 Week Notice	0 days	Thu 4/6/23	Thu 4/6/23
29		24Hr Notice	0 days	Wed 4/12/23	Wed 4/12/23
30		Crommelin Ave, Sparks Way & Budd St	55 days	Thu 4/13/23	Wed 6/28/23



Project: Highway Village Streng
& Replacement water mains
Date: Fri 4/7/23

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

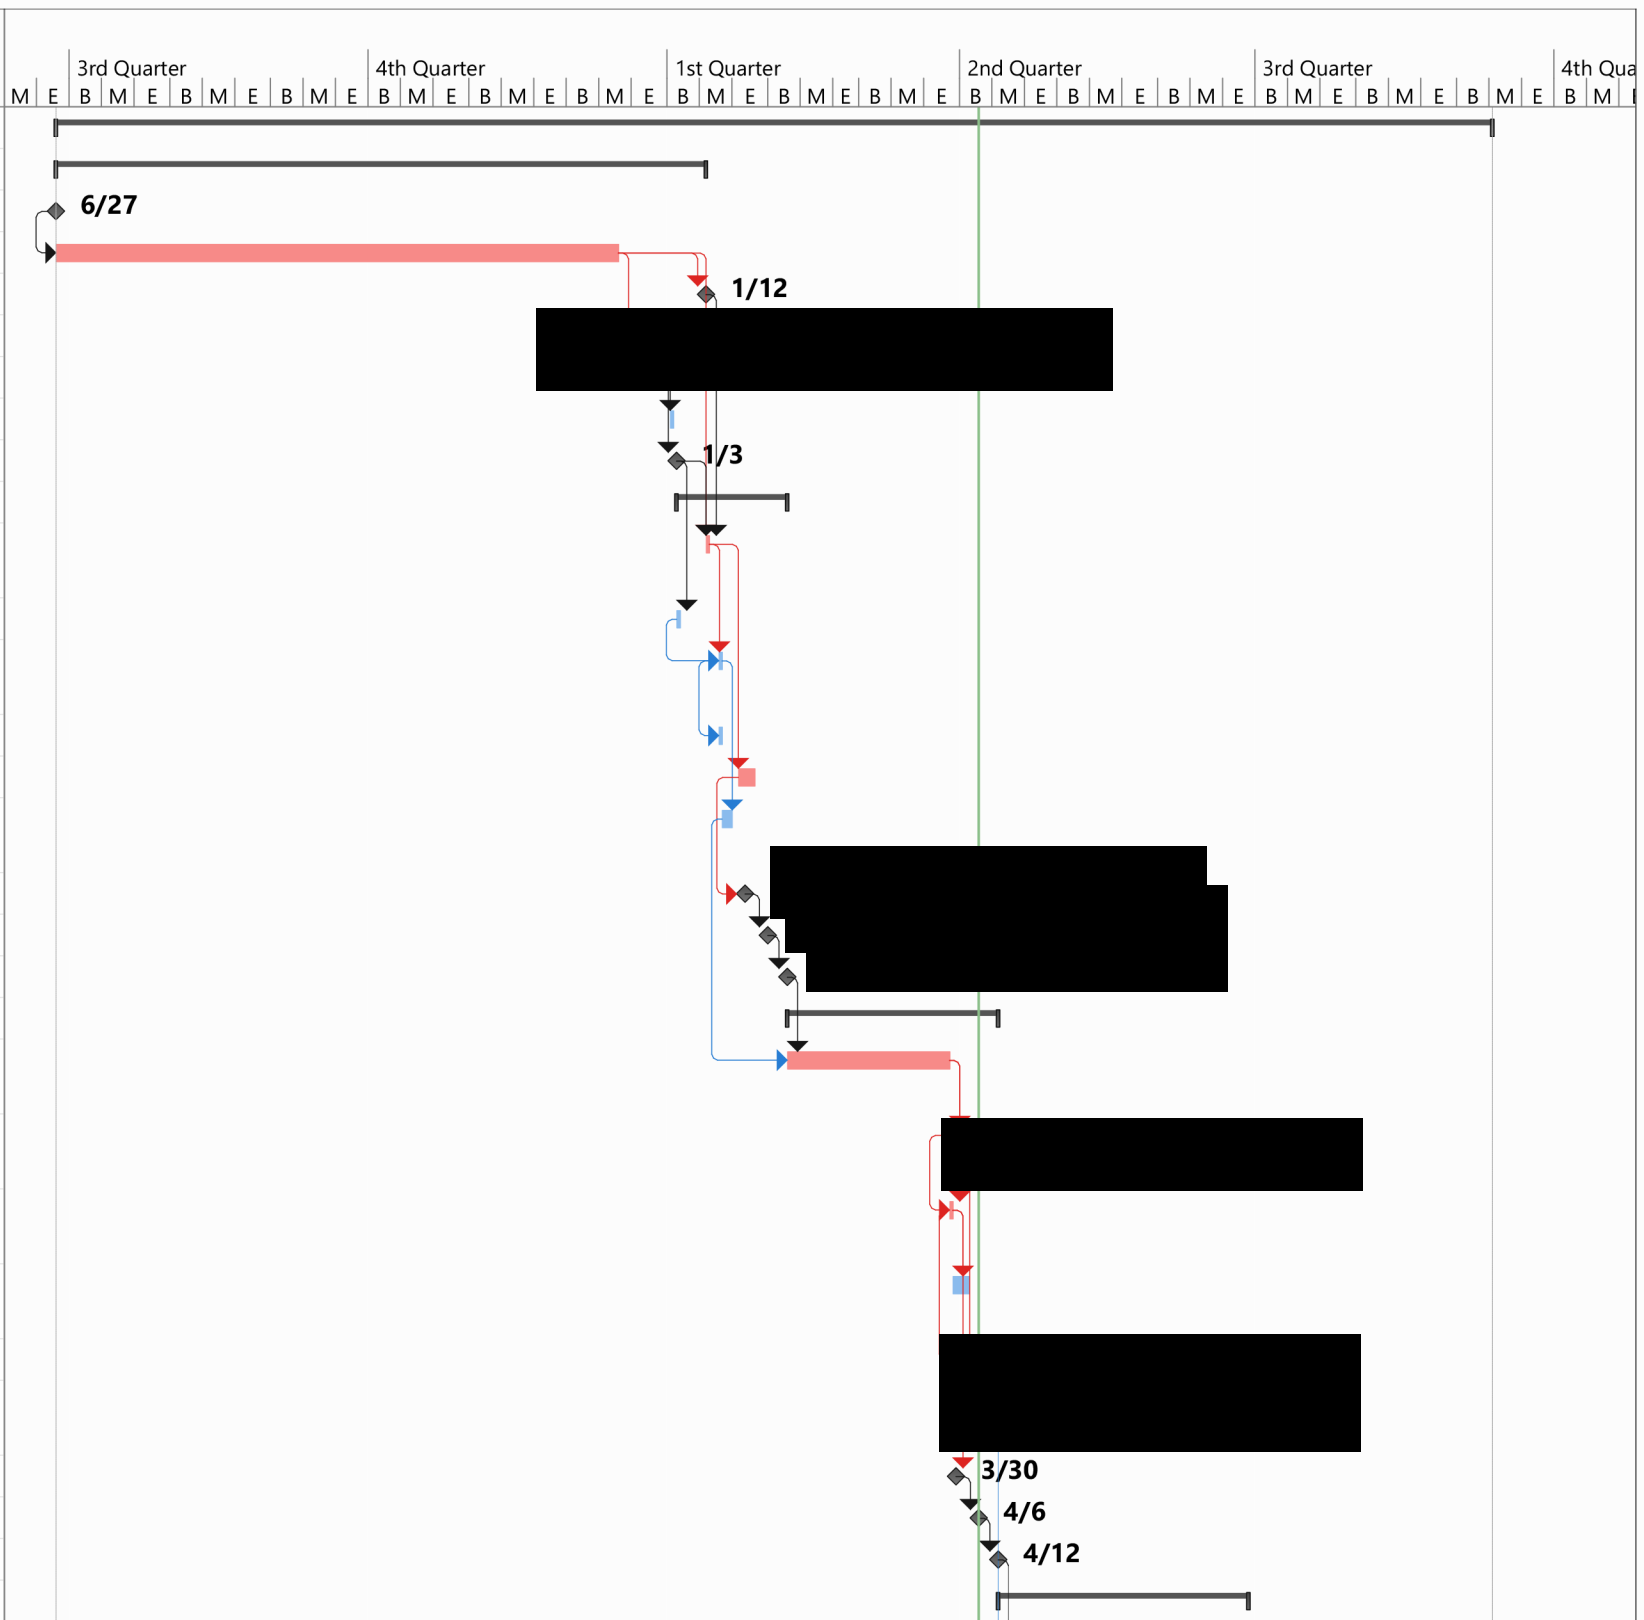

