


CONSTRUCTION ON STATE HIGHWAY VENTURA COUNTIES

Baseline Schedule

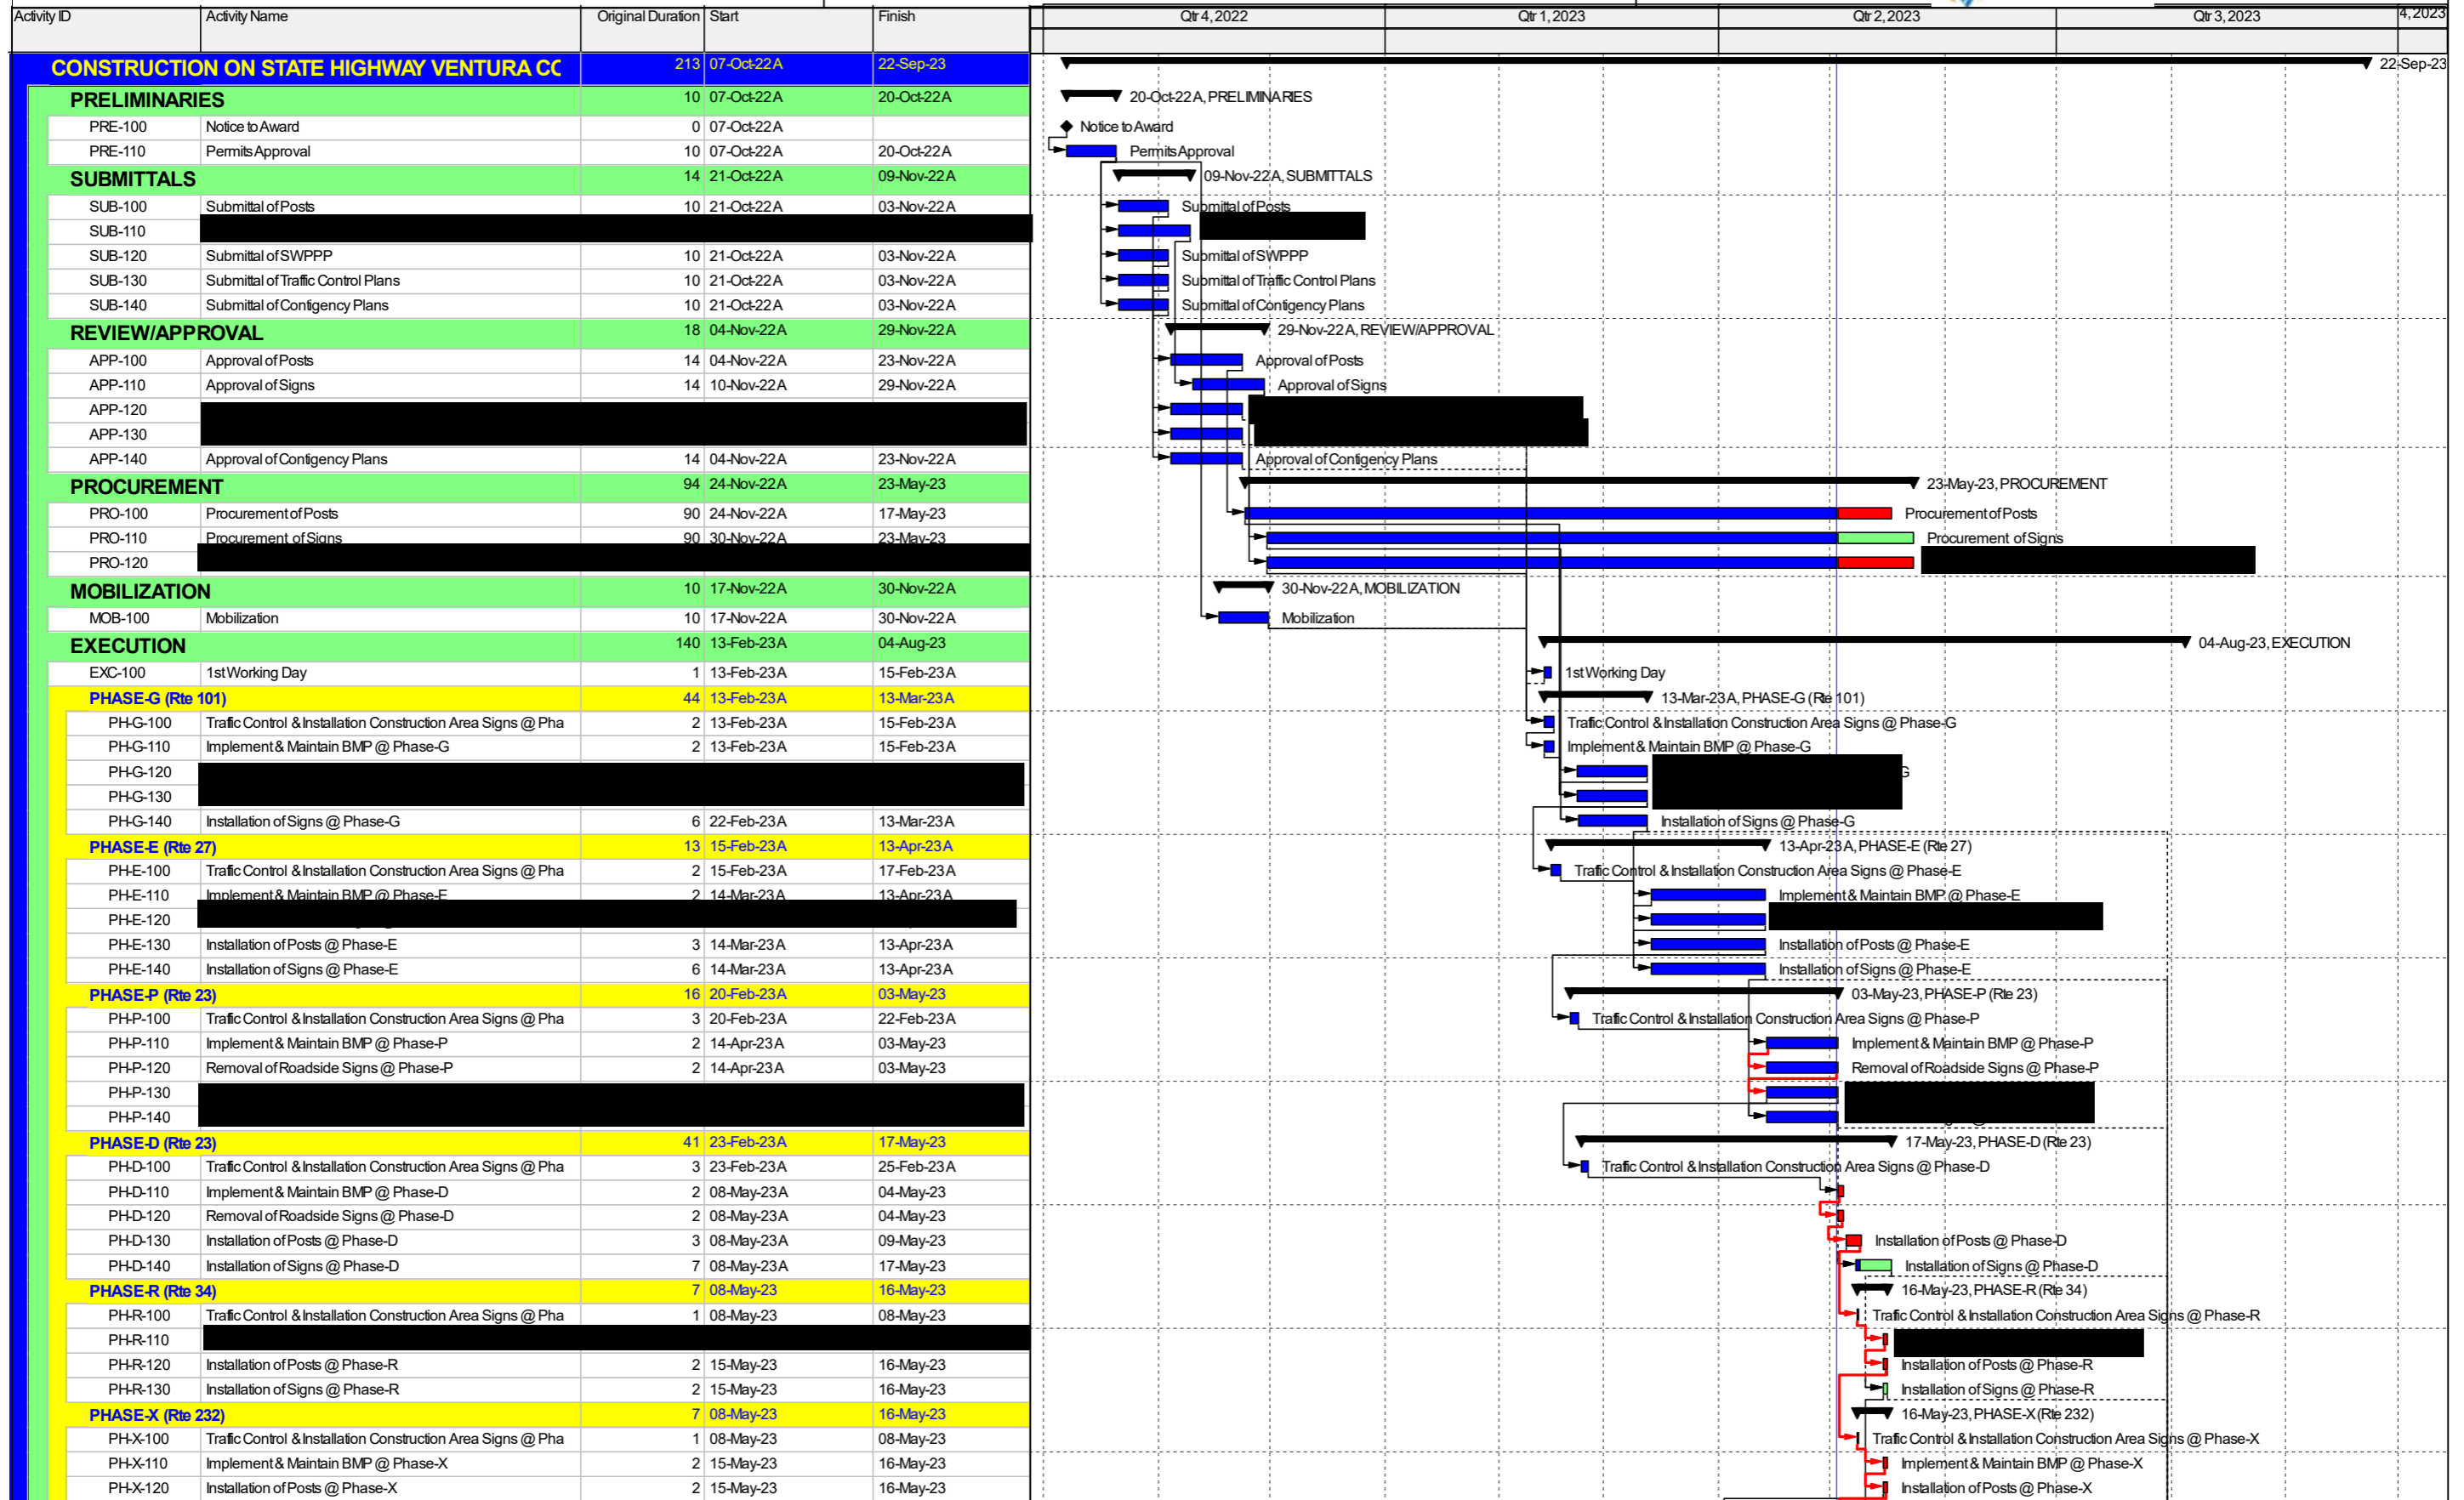


█ Remaining Level of Effort
 █ Actual Level of Effort
 | Actual Work
 | Remaining Work
 █ Critical Remaining W...
 ◆ Milestone

CONSTRUCTION ON STATE HIGHWAY VENTURA COUNTIES

Baseline Schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Qtr 4, 2022	Qtr 1, 2023	Qtr 2, 2023	Qtr 3, 2023	4, 2023
PH-X-130	Installation of Signs @ Phase-X	2	15-May-23	16-May-23					
PHASE-O (Rte 1)									
PH-O-100	Traffic Control & Installation Construction Area Signs @ Pha	3	08-May-23	10-May-23					
PH-O-110	Implement & Maintain BMP @ Phase-O	2	16-May-23	17-May-23					
PH-O-120									
PH-O-130									
PH-O-140									
PHASE-U (Rte 126)									
PH-U-100	Traffic Control & Installation Construction Area Signs @ Pha	2	19-May-23	22-May-23					
PH-U-110	Implement & Maintain BMP @ Phase-U	2	23-May-23	24-May-23					
PH-U-120									
PH-U-130	Installation of Posts @ Phase-U	3	25-May-23	30-May-23					
PH-U-140	Installation of Signs @ Phase-U	5	30-May-23	05-Jun-23					
PHASE-S (Rte 101)									
PH-S-100	Traffic Control & Installation Construction Area Signs @ Pha	1	31-May-23	31-May-23					
PH-S-110	Implement & Maintain BMP @ Phase-S	1	01-Jun-23	01-Jun-23					
PH-S-120	Removal of Roadside Signs @ Phase-S	1	01-Jun-23	01-Jun-23					
PH-S-130	Installation of Posts @ Phase-S	3	02-Jun-23	06-Jun-23					
PH-S-140	Installation of Signs @ Phase-S	4	07-Jun-23	12-Jun-23					
PHASE-V (Rte 150)									
PH-V-100	Traffic Control & Installation Construction Area Signs @ Pha	3	07-Jun-23	09-Jun-23					
PH-V-110	Implement & Maintain BMP @ Phase-V	2	12-Jun-23	13-Jun-23					
PH-V-120									
PH-V-130	Installation of Posts @ Phase-V	3	14-Jun-23	16-Jun-23					
PH-V-140	Installation of Signs @ Phase-V	5	19-Jun-23	23-Jun-23					
PHASE-Q (Rte 33)									
PH-Q-100	Traffic Control & Installation Construction Area Signs @ Pha	3	19-Jun-23	21-Jun-23					
PH-Q-110	Implement & Maintain BMP @ Phase-Q	2	22-Jun-23	23-Jun-23					
PH-Q-120									
PH-Q-130	Installation of Posts @ Phase-Q	5	26-Jun-23	30-Jun-23					
PH-Q-140	Installation of Signs @ Phase-Q	7	29-Jun-23	10-Jul-23					
PHASE-T (Rte 118)									
PH-T-100	Traffic Control & Installation Construction Area Signs @ Pha	2	03-Jul-23	05-Jul-23					
PH-T-110	Implement & Maintain BMP @ Phase-T	2	06-Jul-23	07-Jul-23					
PH-T-120									
PH-T-130	Installation of Posts @ Phase-T	3	10-Jul-23	12-Jul-23					
PH-T-140	Installation of Signs @ Phase-T	4	12-Jul-23	17-Jul-23					
PHASE-I (Rte 118)									
PH-I-100	Traffic Control & Installation Construction Area Signs @ Pha	2	13-Jul-23	14-Jul-23					
PH-I-110	Implement & Maintain BMP @ Phase-I	2	17-Jul-23	18-Jul-23					
PH-I-120									
PH-I-130									
PH-I-140									
PHASE-N (Rte 405)									
PH-N-100	Traffic Control & Installation Construction Area Signs @ Pha	2	24-Jul-23	25-Jul-23					
PH-N-110									
PH-N-120									
PH-N-130	Installation of Posts @ Phase-N	3	28-Jul-23	01-Aug-23					
PH-N-140	Installation of Signs @ Phase-N	4	01-Aug-23	04-Aug-23					
PHASE-L (Rte 170)									
PH-L-100	Traffic Control & Installation Construction Area Signs @ Pha	2	07-Apr-23A	10-Apr-23A					
PH-L-110	Implement & Maintain BMP @ Phase-L	2	11-Apr-23A	12-Apr-23A					
PH-L-120	Removal of Roadside Signs @ Phase-L	2	11-Apr-23A	12-Apr-23A					
PH-L-130	Installation of Posts @ Phase-L	3	13-Apr-23A	17-Apr-23A					
PH-L-140	Installation of Signs @ Phase-L	6	17-Apr-23A	24-Apr-23A					
PHASE-A (Rte 2)									
PH-A-100									
PH-A-110									
PH-A-120									

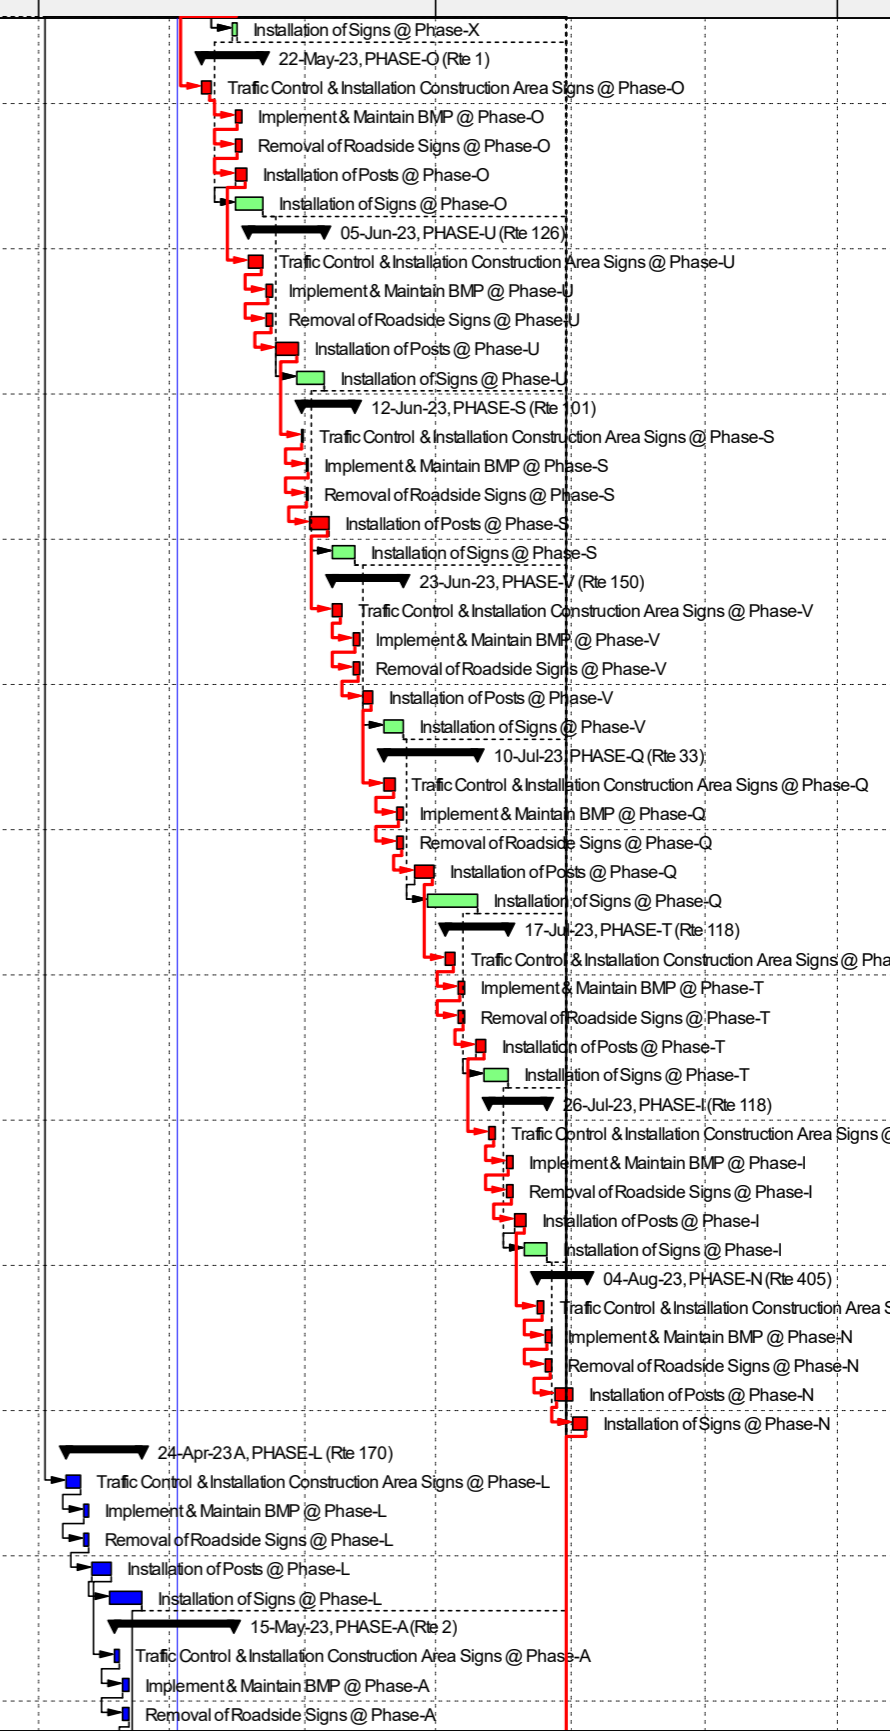

█ Remaining Level of Effort
 █ Actual Level of Effort
 | Actual Work
 | Remaining Work
 █ Critical Remaining W...
 ◆ Milestone

CONSTRUCTION ON STATE HIGHWAY VENTURA COUNTIES

Baseline Schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Qtr 4, 2022	Qtr 1, 2023	Qtr 2, 2023	Qtr 3, 2023	4, 2023
PHA-130	Installation of Posts @ Phase-A	3	24-Apr-23A	26-Apr-23A					
PHA-140	Installation of Signs @ Phase-A	5	27-Apr-23A	15-May-23					
PHASE-M (Rte 210)									
PHM-100	Traffic Control & Installation Construction Area Signs @ Pha	2	27-Apr-23A	28-Apr-23A					
PHM-110	Implement & Maintain BMP @ Phase-M	2	01-May-23A	02-May-23A					
PHM-120									
PHM-130									
PHM-140	Installation of Signs @ Phase-M	5	17-May-23	23-May-23					
PHASE-F (Rte 90)									
PHF-100	Traffic Control & Installation Construction Area Signs @ Pha	2	18-May-23	19-May-23					
PHF-110									
PHF-120									
PHF-130	Installation of Posts @ Phase-F	3	23-May-23	25-May-23					
PHF-140	Installation of Signs @ Phase-F	4	26-May-23	01-Jun-23					
PHASE-H (Rte 105)									
PHH-100	Traffic Control & Installation Construction Area Signs @ Pha	2	26-May-23	30-May-23					
PHH-110									
PHH-120									
PHH-130									
PHASE-B (Rte 5)									
PHB-100	Traffic Control & Installation Construction Area Signs @ Pha	2	05-Jun-23	06-Jun-23					
PHB-110	Implement & Maintain BMP @ Phase-B	2	05-Jun-23	06-Jun-23					
PHB-120									
PHB-130									
PHB-140									
PHASE-J (Rte 126)									
PHJ-100	Traffic Control & Installation Construction Area Signs @ Pha	2	12-Jun-23	13-Jun-23					
PHJ-110									
PHJ-120									
PHJ-130									
PHASE-C (Rte 14)									
PHC-100	Traffic Control & Installation Construction Area Signs @ Pha	2	19-Jun-23	20-Jun-23					
PHC-110	Implement & Maintain BMP @ Phase-C	1	21-Jun-23	21-Jun-23					
PHC-120									
PHC-130									
PHC-140									
PHASE-K (Rte 138)									
PHK-100	Traffic Control & Installation Construction Area Signs @ Pha	2	27-Jun-23	28-Jun-23					
PHK-110	Implement & Maintain BMP @ Phase-K	1	29-Jun-23	29-Jun-23					
PHK-120									
PHK-130									
PHK-140									
CLOSE OUT									
CO-100	Substantial Completion	0	04-Aug-23	04-Aug-23					
CO-110									
CO-120									
CO-130									
CO-140	Final Clean	7	05-Sep-23	13-Sep-23					
CO-150	Final Inspection	3	14-Sep-23	18-Sep-23					
CO-160	Demobilize	4	19-Sep-23	22-Sep-23					
CO-170	Final Completion	0		22-Sep-23					



■ Remaining Level of Effort
 ■ Actual Level of Effort
 ■ Critical Remaining W...
 | Actual Work
 | Remaining Work
 ◆ Milestone
